

Salt Lake City Cemetery
Roadway and Irrigation Improvements
Monthly Project Report
July 2025

Prepared by:



Table of Contents

1.	Executive Summary
2.	Project Photographs
3.	Budget/Cost Summary
4.	Schedule Summary
5.	Next Month "Look-ahead"
	Attachment "A" – Project Budget
	Attachment "B" – Project Schedule



1. Executive Summary

The SLC City Cemetery Roadway and Irrigation Improvements project has continued from June with the placing of curb and gutter in Phases 11 and 12. Paving has been completed in Phase 11. Phases 1, 2, 3A, 4, 5, 6, 7, 8, 9, and 10 are now open. Installation of service laterals has been completed in all phases of the project. MC Green has completed the swap of the water meter and installation of the new backflow preventer and testing of this line. Water service was off after installation due to bacteriological testing and was not returned by the end of the month. The project is on schedule to finish the roadways and roadway irrigation around the middle of August. The slight delay is due to changing the concrete crew from an internal MC Green crew to WM Green. WM Green has continued to show themselves capable of keeping up with the schedule demands of MC Green in the placement of concrete. Landscaping continues working in the Plat areas with trenching, installing pipe, and installing irrigation devices. An additional landscaping company was brought in by MC Green to assist and ensure the project finishes on-time. Sod watering continues to be a concern, the landscaper and MC Green are consistently searching for new ways to accomplish the watering. Discussions have begun on how to revive the sod once the water is back in service and more controllers are available for manual watering. We will either need to resod or overseed several of the project Plats. MOCA has continued to be present for all major concrete pours and weekly meetings continue to be held every Tuesday.

MOCA activities for the project include:

- RFI/Submittal coordination
- Arrange and participate in onsite meetings (Weekly meeting and Historic Wall review)
- Arrange and participate in virtual meetings
- Assist with ProCore
- Produce meeting agendas and minutes
- Continue to work with the contractor on the schedule
- Verify the accuracy of the pay requests
- Observed concrete pours of curb and gutter and pavement

2. Project Photographs

2.1. Images of City Cemetery Roadway and Irrigation Improvements





Paving, Phase 11




Curb in Phase 11



Curb in Phase 12



Paving, Phase 12

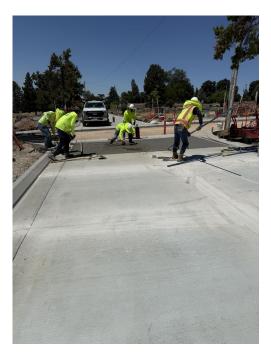

Paving near manholes in Phase 11



Paving, Phase 12




Pavement after cutting, Phase 11



Cutting out the old T junction from the water main



Fitting the new T junction and valves

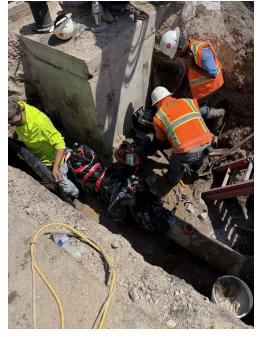

Connecting the water main to the new meter



Paving, Phase 12



Connecting the water main to the backflow preventer







Concrete form in Phase 12

3. Budget/Cost Summary

Attachment "A" has been updated for the month of June. Attachment "A" illustrates the overall budget and its distribution into specific line items. As invoices are received, they will be entered into ProCore, Salt Lake City's Project Management Software and be reflected in this table. This table also tracks Committed Costs and any Change Orders.

4. Schedule Summary

This Project is scheduled to be completed in two Work Sequences due to funding requirements. Work Sequence 1 will terminate at midnight on the 30th of August 2025. Work Sequence 2 will terminate at midnight on the 31st of May 2025.

The current schedule submitted by MC Green is attached in Attachment "B". This is an updated schedule based on the start date of 12/2/24. This new schedule has completion estimated to be mid-September with directional boring proving to shorten the overall duration.

5. Next Month "Look-ahead"

Activities anticipated to occur next month include:

- Paving
- Irrigation



• Concrete Punchlist items

END OF REPORT



Budget Code	Budget Code Description	Vendor	Item	Description	Detail Type	Original Budget Amount	Budget Modifications	Approved COs	Pending Budget Changes	Committed Costs	Direct Costs	Pending Cost Changes	Forecast To Complete
77-77247.CIVIL-2700-000-00 02.SC	Donation Cost Center.Contingency Allowance.Soft Costs	None	Original Budget		Original Budget Amount	\$10,429.00							
77-77247.CIVIL-2700-000-00 02.SC	Donation Cost Center.Contingency Allowance.Soft Costs	None			Automatic Forecast								\$10,429.00
77-77247.OC-2313-329.SC	Donation Cost Center.Manage Consultant Projects (Inhouse).Soft Costs	None	Original Budget		Original Budget Amount	\$2,301.00							
77-77247.OC-2313-329.SC	Donation Cost Center.Manage Consultant Projects (In- house).Soft Costs	None			Automatic Forecast								\$2,301.00
77-77247.OC-2329-679.SC	Donation Cost Center.Design (Consultant).Soft Costs	None	Original Budget		Original Budget Amount	\$980,000.00							
77-77247.OC-2329-679.SC	Donation Cost Center.Design (Consultant).Soft Costs	Civil Solutions Group, Inc. (CSG)	#WD SCON-00001288: City Cemetery Roadway & Irrigation Improvements - Design & CA Services	Design Phase Portion. Donation.	Commitment Contract					\$540,205.00			
77-77247.OC-2329-679.SC	Donation Cost Center.Design (Consultant).Soft Costs	Civil Solutions Group, Inc. (CSG)	#WD SCON-00001288: City Cemetery Roadway & Irrigation Improvements - Design & CA Services	Predesign. Phase 1 Existing Conditions, Phase 2, Phase 3. Donation.	Commitment Contract					\$439,795.00			
77-77247.OC-2329-679.SC	Donation Cost Center.Design (Consultant).Soft Costs	None			Automatic Forecast								\$0.00
77-77247.OC-2329-682.SC	Donation Cost Center.Planning & Studies (Consultant).Soft Costs	None	Original Budget		Original Budget Amount	\$7,270.00							
77-77247.OC-2329-682.SC	Donation Cost Center.Planning & Studies (Consultant).Soft Costs	Roadway Asset Services, LLC (RAS)	#SCON-00001341: City Cemetery Roadway & Irrigation Improvements		Commitment Contract					\$7,270.00			
77-77247.OC-2329-682.SC	Donation Cost Center.Planning & Studies (Consultant).Soft Costs	None			Automatic Forecast								\$0.00
PRJ-230007-83-23213.CIVIL-2700-000-00 01.CONST	Revenue Bond Cost Center.Construction Allowance.Construction	None	Original Budget		Original Budget Amount	\$9,317,999.00							
PRJ-230007-83-23213.CIVIL-2700-000-00 01.CONST	Revenue Bond Cost Center.Construction Allowance.Construction	& Sons, Inc.	#WD SCON-00002441: City Cemetery Roadway & Irrigation Improvements - PRK23013	MCG Rev. Bond	Commitment Contract					\$9,317,999.00			
PRJ-230007-83-23213.CIVIL-2700-000-00 01.CONST	Revenue Bond Cost Center.Construction Allowance.Construction	None			Automatic Forecast								\$0.00
PRJ-230007-83-23213.CIVIL-2700-000-00 02.CONST	Revenue Bond Cost Center.Contingency Allowance.Construction	None	Original Budget		Original Budget Amount	\$86,000.00							
PRJ-230007-83-23213.CIVIL-2700-000-00 02.CONST	Revenue Bond Cost Center.Contingency Allowance.Construction		#005: Saddle Replacement	Saddle Replacement	Commitment Potential Change Order					\$45,078.24			
PRJ-230007-83-23213.CIVIL-2700-000-00 02.CONST	Revenue Bond Cost Center.Contingency Allowance.Construction		#004: Undocumented Remains	Undocumented Remains	Commitment Potential Change Order					\$2,048.06			
PRJ-230007-83-23213.CIVIL-2700-000-00	Revenue Bond Cost	M.C. Green	#003: Conduit Fix in Phase 1	Conduit Fix	Commitment					\$2,220.29			
Report Grand Total					\$	14,527,708.51	\$0.00	\$0.00	\$0.00	\$12,954,112.83	\$124,472.07	\$0.00	\$1,449,123.61


						Original							
Budget Code	Budget Code Description	Vendor	Item	Description	Detail Type		Budget Modifications	Approved COs	Pending Budget Changes	Committed Costs	Direct Costs	Pending Cost Changes	Forecast To Complete
02.CONST	Center.Contingency Allowance.Construction	& Sons, Inc. (MCG)			Potential Change Order								
PRJ-230007-83-23213.CIVIL-2700-000-00 02.CONST	Revenue Bond Cost Center.Contingency Allowance.Construction		#002: Unmarked Conduit Phase 3B	Conduit Repair	Commitment Potential Change Order					\$3,379.24			
PRJ-230007-83-23213.CIVIL-2700-000-00 02.CONST	Revenue Bond Cost Center.Contingency Allowance.Construction	M.C. Green & Sons, Inc. (MCG)	#001: Unknown Concrete Storm Drain Structure	Lower Structure	Commitment Potential Change Order					\$2,626.51			
PRJ-230007-83-23213.CIVIL-2700-000-00 02.CONST	Revenue Bond Cost Center.Contingency Allowance.Construction	None			Automatic Forecast								\$30,647.66
PRJ-230007-83-23213.CIVIL-2700-32-01 9311.CONST	Revenue Bond Cost Center.Tree Pruning.Construction	None	Original Budget		Original Budget Amount	\$24,750.00							
PRJ-230007-83-23213.CIVIL-2700-32-01 9311.CONST	Revenue Bond Cost Center.Tree Pruning.Construction	SuperTrees Utah, LLC	#SCON-00001575 CA-003038: PRK23013 City Cemetery - Tree Pruning	Cemetery tree pre-pruning.	Commitment Contract					\$24,749.99			
PRJ-230007-83-23213.CIVIL-2700-32-01 9311.CONST	Revenue Bond Cost Center.Tree Pruning.Construction	None			Automatic Forecast								\$0.01
PRJ-230007-83-23213.OC-0600-675.SC	Revenue Bond Cost Center.Stormwater Drainage Fee.Soft Costs	None	Original Budget		Original Budget Amount	\$11,594.00							
PRJ-230007-83-23213.OC-0600-675.SC	Revenue Bond Cost Center.Stormwater Drainage Fee.Soft Costs	Salt Lake City Public Utilities	Expense: PUT2024-00929 Water and Drainage Permit Fees. Two invoice number son one permit fee form. Invoice 1990656 \$34,967.28. Meter and Drainage Invoice 1990475.	Storm water drainage fee. Variance for impacted area only instead of full area of 4 parcesl.	Direct Cost						\$11,594.00		
PRJ-230007-83-23213.OC-0600-675.SC	Revenue Bond Cost Center.Stormwater Drainage Fee.Soft Costs	None			Automatic Forecast								\$0.00
PRJ-230007-83-23213.OC-0600-677.SC	Revenue Bond Cost Center.Miscellaneous (Printing, etc.).Soft Costs	None	Original Budget		Original Budget Amount	\$1,500.00							
PRJ-230007-83-23213.OC-0600-677.SC	Revenue Bond Cost Center.Miscellaneous (Printing, etc.).Soft Costs	The Salt Lake Tribune	Invoice #2024ci-13500: Const Adv. 7/7-7/ 21/24	tribune const adv	Direct Cost						\$804.20		
PRJ-230007-83-23213.OC-0600-677.SC	Revenue Bond Cost Center.Miscellaneous (Printing, etc.).Soft Costs	The Salt Lake Tribune	Invoice #2024ci-12759:	GC Prequalification Solicitation Adv.	Direct Cost						\$426.20		
PRJ-230007-83-23213.OC-0600-677.SC	Revenue Bond Cost Center.Miscellaneous (Printing, etc.).Soft Costs	Rocky Mountain Transit Instruments	Invoice #156359: Survey flags etc, mark design irr heads to find routes around graves/ec.	Survey flags, etc.	Direct Cost						\$83.21		
PRJ-230007-83-23213.OC-0600-677.SC	Revenue Bond Cost Center.Miscellaneous (Printing, etc.).Soft Costs	None			Automatic Forecast								\$186.39
PRJ-230007-83-23213.OC-0600-687.SC	Revenue Bond Cost Center.Water.Soft Costs	None	Original Budget		Original Budget Amount	\$111,564.46							
PRJ-230007-83-23213.OC-0600-687.SC	Revenue Bond Cost Center.Water.Soft Costs	Salt Lake City Public Utilities	Expense: PUT2024-00929 Water and Drainage Permit Fees. Two invoice number son one permit fee form.	6" Meter, Water Resource Fee, and Kill existing water service	Direct Cost						\$111,564.46		
Report Grand Total						\$14,527,708.51	\$0.00	\$0.00	\$0.00	\$12,954,112.83	\$124,472.07	\$0.00	\$1,449,123.61

Budget Code	Budget Code Description	Vendor	Item	Description	Detail Type	Original Budget Amount	Budget Modifications	Approved COs	Pending Budget Changes	Committed Costs	Direct Costs	Pending Cost Changes	Forecast To Complete
			Invoice 1990656 \$34,967.28. Meter and Drainage Invoice 1990475.										
PRJ-230007-83-23213.OC-0600-687.SC	Revenue Bond Cost Center.Water.Soft Costs	None			Automatic Forecast								\$0.00
PRJ-230007-83-23213.OC-2313-329.SC	Revenue Bond Cost Center.Manage Consultant Projects (Inhouse).Soft Costs	None	Original Budget		Original Budget Amount	\$46,091.50							
PRJ-230007-83-23213.OC-2313-329.SC	Revenue Bond Cost Center.Manage Consultant Projects (Inhouse).Soft Costs	None			Automatic Forecast								\$46,091.50
PRJ-230007-83-23213.OC-2329-000.SC	Revenue Bond Cost Center.Consultant Engineering Allowance.Soft Costs	None	Original Budget		Original Budget Amount	\$383,902.00							
PRJ-230007-83-23213.OC-2329-000.SC	Revenue Bond Cost Center.Consultant Engineering Allowance.Soft Costs	MOCA Systems, Inc.	#WD SCON-00000761 (line 6), 06-S-22-4032, State Contract MA013, : City Cemetery Roadway and Irrigation Improvements	Project Management Services	Commitment Contract					\$306,902.00			
PRJ-230007-83-23213.OC-2329-000.SC	Revenue Bond Cost Center.Consultant Engineering Allowance.Soft Costs	None			Automatic Forecast								\$77,000.00
PRJ-230007-83-23213.OC-2329-679.SC	Revenue Bond Cost Center.Design (Consultant).Soft Costs	None	Original Budget		Original Budget Amount	\$875,761.00							
PRJ-230007-83-23213.OC-2329-679.SC	Revenue Bond Cost Center.Design (Consultant).Soft Costs	Civil Solutions Group, Inc. (CSG)	#001: Add Service 1	Part 6. Extend construction period due to flexibility in state fund deadline 92,397+23,853=116,250	Commitment Potential Change Order					\$23,853.00			
PRJ-230007-83-23213.OC-2329-679.SC	Revenue Bond Cost Center.Design (Consultant).Soft Costs	Civil Solutions Group, Inc. (CSG)	#001: Add Service 1	Part 5a. Design deduct. Reduced construction budget. Original const. budget and CO1 Part 1 const. budget reconciliation. Deduct from Part 1a \$-21,468.56 final, plan/permitting, bidding.	Commitment Potential Change Order					(\$21,468.00)			
PRJ-230007-83-23213.OC-2329-679.SC	Revenue Bond Cost Center.Design (Consultant).Soft Costs	Civil Solutions Group, Inc. (CSG)	#001: Add Service 1	Part 5b. CA deduct. Reduced Construction budget, budget reconciliation. Deduct from Part 1b. \$-23,853.00 const	Commitment Potential Change Order					(\$23,853.00)			
PRJ-230007-83-23213.OC-2329-679.SC	Revenue Bond Cost Center.Design (Consultant).Soft Costs	Civil Solutions Group, Inc. (CSG)	#001: Add Service 1	Part 1b. CA, due to added state funds.	Commitment Potential Change Order					\$74,775.00			
PRJ-230007-83-23213.OC-2329-679.SC	Revenue Bond Cost Center.Design (Consultant).Soft Costs	Civil Solutions Group, Inc. (CSG)	#001: Add Service 1	Part 4. Redesign. Change to Concrete and reduce project area in lieu of asphalt and storm drain. Partial 11th ave storm water evaluation.	Commitment Potential Change Order					\$97,600.00			
PRJ-230007-83-23213.OC-2329-679.SC	Revenue Bond Cost Center.Design (Consultant).Soft Costs	Civil Solutions Group, Inc. (CSG)	#001: Add Service 1	Part 3. Expedite design to 4th S area.	Commitment Potential Change Order					\$73,154.00			
PRJ-230007-83-23213.OC-2329-679.SC	Revenue Bond Cost Center.Design (Consultant).Soft Costs	Civil Solutions Group, Inc. (CSG)	#001: Add Service 1	Part 2. Deduct. Original "Misc. Items, Phased Design", Procore SOV4, no longer required.	Commitment Potential Change Order					(\$123,154.00)			
PRJ-230007-83-23213.OC-2329-679.SC	Revenue Bond Cost Center.Design (Consultant).Soft Costs	Civil Solutions Group, Inc. (CSG)	#001: Add Service 1	Part 1a. Design, due to added state funds	Commitment Potential Change Order					\$224,325.00			
PRJ-230007-83-23213.OC-2329-679.SC	Revenue Bond Cost Center.Design	Civil Solutions	#WD SCON-00001288: City Cemetery Roadway & Irrigation Improvements -	Miscellaneous. BOND.	Commitment Contract					\$44,475.00			
Report Grand Total						\$14,527,708.51	\$0.00	\$0.00	\$0.00	\$12,954,112.83	\$124,472.07	\$0.00	\$1,449,123.61


Budget Code	Budget Code Description	Vendor	Item	Description	Detail Type	Original Budget Amount	Budget Modifications	Approved COs	Pending Budget Changes	Committed Costs	Direct Costs	Pending Cost Changes	Forecast To Complete
	(Consultant).Soft Costs	Group, Inc. (CSG)	Design & CA Services										
PRJ-230007-83-23213.OC-2329-679.SC	Revenue Bond Cost Center.Design (Consultant).Soft Costs	Civil Solutions Group, Inc. (CSG)	#WD SCON-00001288: City Cemetery Roadway & Irrigation Improvements - Design & CA Services	Construction Administration. BOND.	Commitment Contract					\$228,064.00			
PRJ-230007-83-23213.OC-2329-679.SC	Revenue Bond Cost Center.Design (Consultant).Soft Costs	Civil Solutions Group, Inc. (CSG)	#WD SCON-00001288: City Cemetery Roadway & Irrigation Improvements - Design & CA Services	Miscellaneous Scope. BOND.	Commitment Contract					\$134,004.00			
PRJ-230007-83-23213.OC-2329-679.SC	Revenue Bond Cost Center.Design (Consultant).Soft Costs	Civil Solutions Group, Inc. (CSG)	#WD SCON-00001288: City Cemetery Roadway & Irrigation Improvements - Design & CA Services	Design Phase Portion. BOND.	Commitment Contract					\$143,986.00			
PRJ-230007-83-23213.OC-2329-679.SC	Revenue Bond Cost Center.Design (Consultant).Soft Costs	None			Automatic Forecast								\$0.00
PRJ-230007-83-23213.OC-2329-681.SC	Revenue Bond Cost Center.Materials Testing (Consultant).Soft Costs	None	Original Budget		Original Budget Amount	\$158,600.00							
PRJ-230007-83-23213.OC-2329-681.SC	Revenue Bond Cost Center.Materials Testing (Consultant).Soft Costs	Terracon Consultants, Inc.	#002: Reduce estimated contract amount.	Reduce estimated testing budget total	Commitment Potential Change Order					(\$20,000.00)			
PRJ-230007-83-23213.OC-2329-681.SC	Revenue Bond Cost Center.Materials Testing (Consultant).Soft Costs	Terracon Consultants, Inc.	#001: Reduce estimated contract amount.	Reduce estimated budget total	Commitment Potential Change Order					(\$15,000.00)			
PRJ-230007-83-23213.OC-2329-681.SC	Revenue Bond Cost Center.Materials Testing (Consultant).Soft Costs	Terracon Consultants, Inc.	#SCON-00001695 06-2-23-4789 ONC22065: PRK23013 City Cemetery - Construction Materials Testing	Construction Materials Testing	Commitment Contract					\$193,600.00			
PRJ-230007-83-23213.OC-2329-681.SC	Revenue Bond Cost Center.Materials Testing (Consultant).Soft Costs	None			Automatic Forecast								\$0.00
PRJ-230007-83-23213.OC-2329-685.SC	Revenue Bond Cost Center.Contract Admin, Testing & Insp. (Consultant).Soft Costs	None	Original Budget		Original Budget Amount	\$193,600.00							
PRJ-230007-83-23213.OC-2329-685.SC	Revenue Bond Cost Center.Contract Admin, Testing & Insp. (Consultant).Soft Costs	None			Automatic Forecast								\$193,600.00
PRJ-230007-FY2B5A4.CIVIL-2700-000-00 01.CONST	State Funding 3000 CIP GF.Construction Allowance.Construction	None	Original Budget		Original Budget Amount	\$1,086,681.50							
PRJ-230007-FY2B5A4.CIVIL-2700-000-00 01.CONST	State Funding 3000 CIP GF.Construction Allowance.Construction	& Sons, Inc.	#WD SCON-00002441: City Cemetery Roadway & Irrigation Improvements - PRK23013	MCG State	Commitment Contract					\$1,086,681.50			
PRJ-230007-FY2B5A4.CIVIL-2700-000-00 01.CONST	State Funding 3000 CIP GF.Construction Allowance.Construction	None			Automatic Forecast								\$0.00
PRJ-230007-FY2B5A4.CIVIL-2700-000-00 02.CONST	State Funding 3000 CIP GF.Contingency Allowance.Construction	None	Original Budget		Original Budget Amount	\$1,040,468.05							
PRJ-230007-FY2B5A4.CIVIL-2700-000-00 02.CONST	State Funding 3000 CIP GF.Contingency Allowance.Construction	None			Automatic Forecast								\$1,040,468.05
PRJ-230007-FY2B5A4.OC-2329-679.SC	State Funding 3000 CIP	None	Original Budget		Original	\$92,397.00							
Report Grand Total						\$14,527,708.51	\$0.00	\$0.00	\$0.00	\$12,954,112.83	\$124,472.07	\$0.00	\$1,449,123.61

Budget Code	Budget Code Description	Vendor	Item	Description	Detail Type	Original Budget Amount	Budget Modifications	Approved COs	Pending Budget Changes	Committed Costs	Direct Costs	Pending Cost Changes	Forecast To Complete
	GF.Design (Consultant).Soft Costs				Budget Amount								
PRJ-230007-FY2B5A4.OC-2329-679.SC	State Funding 3000 CIP GF.Design (Consultant).Soft Costs	Civil Solutions Group, Inc. (CSG)	#001: Add Service 1	Part 6. Extend construction period due to flexibility in state fund deadline.	Commitment Potential Change Order					\$92,397.00			
PRJ-230007-FY2B5A4.OC-2329-679.SC	State Funding 3000 CIP GF.Design (Consultant).Soft Costs	None			Automatic Forecast								\$0.0
PRJ-230007-FY2B5A4.OC-2329-681.SC	State Funding 3000 CIP GF.Materials Testing (Consultant).Soft Costs	None	Original Budget		Original Budget Amount	\$48,400.00							
PRJ-230007-FY2B5A4.OC-2329-681.SC	State Funding 3000 CIP GF.Materials Testing (Consultant).Soft Costs	Consultants	#SCON-00001695 06-2-23-4789 , ONC22065: PRK23013 City Cemetery - Construction Materials Testing	Construction Materials Testing	Commitment Contract					\$48,400.00			
PRJ-230007-FY2B5A4.OC-2329-681.SC	State Funding 3000 CIP GF.Materials Testing (Consultant).Soft Costs				Automatic Forecast								\$0.0
PRJ-230007-FY2B5A4.OC-2329-685.SC	State Funding 3000 CIP GF.Contract Admin, Testing & Insp. (Consultant).Soft Costs	None	Original Budget		Original Budget Amount	\$48,400.00							
PRJ-230007-FY2B5A4.OC-2329-685.SC	State Funding 3000 CIP GF.Contract Admin, Testing & Insp. (Consultant).Soft Costs	None			Automatic Forecast								\$48,400.
Report Grand Total						\$14,527,708.51	\$0.00	\$0.00	\$0.00	\$12,954,112.83	\$124,472.07	\$0.00	\$1,449,123.


smartsheet

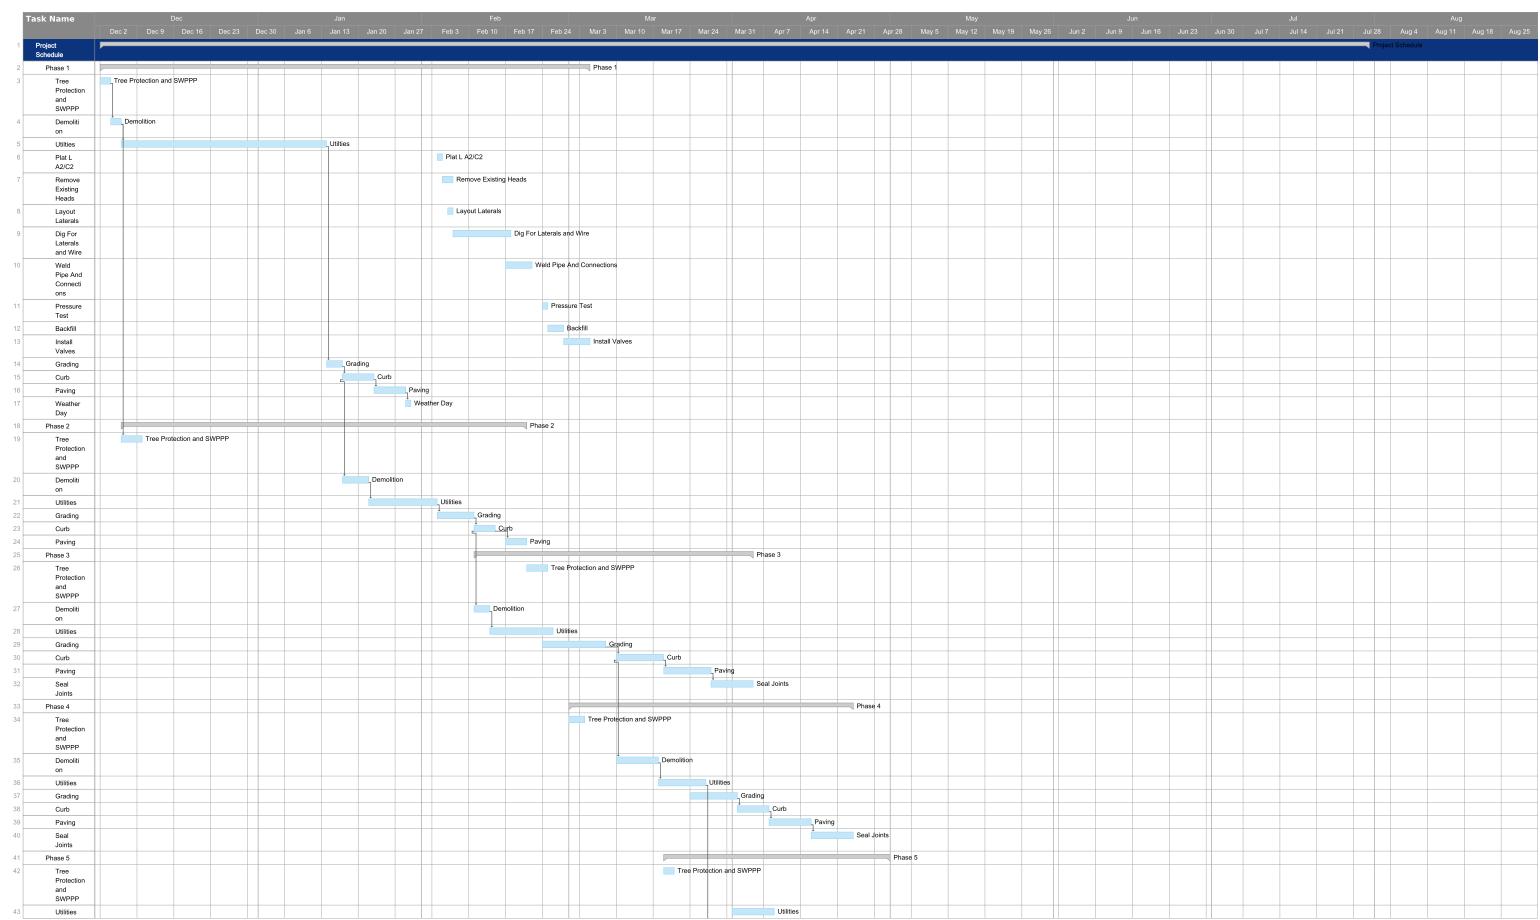

Attachment B

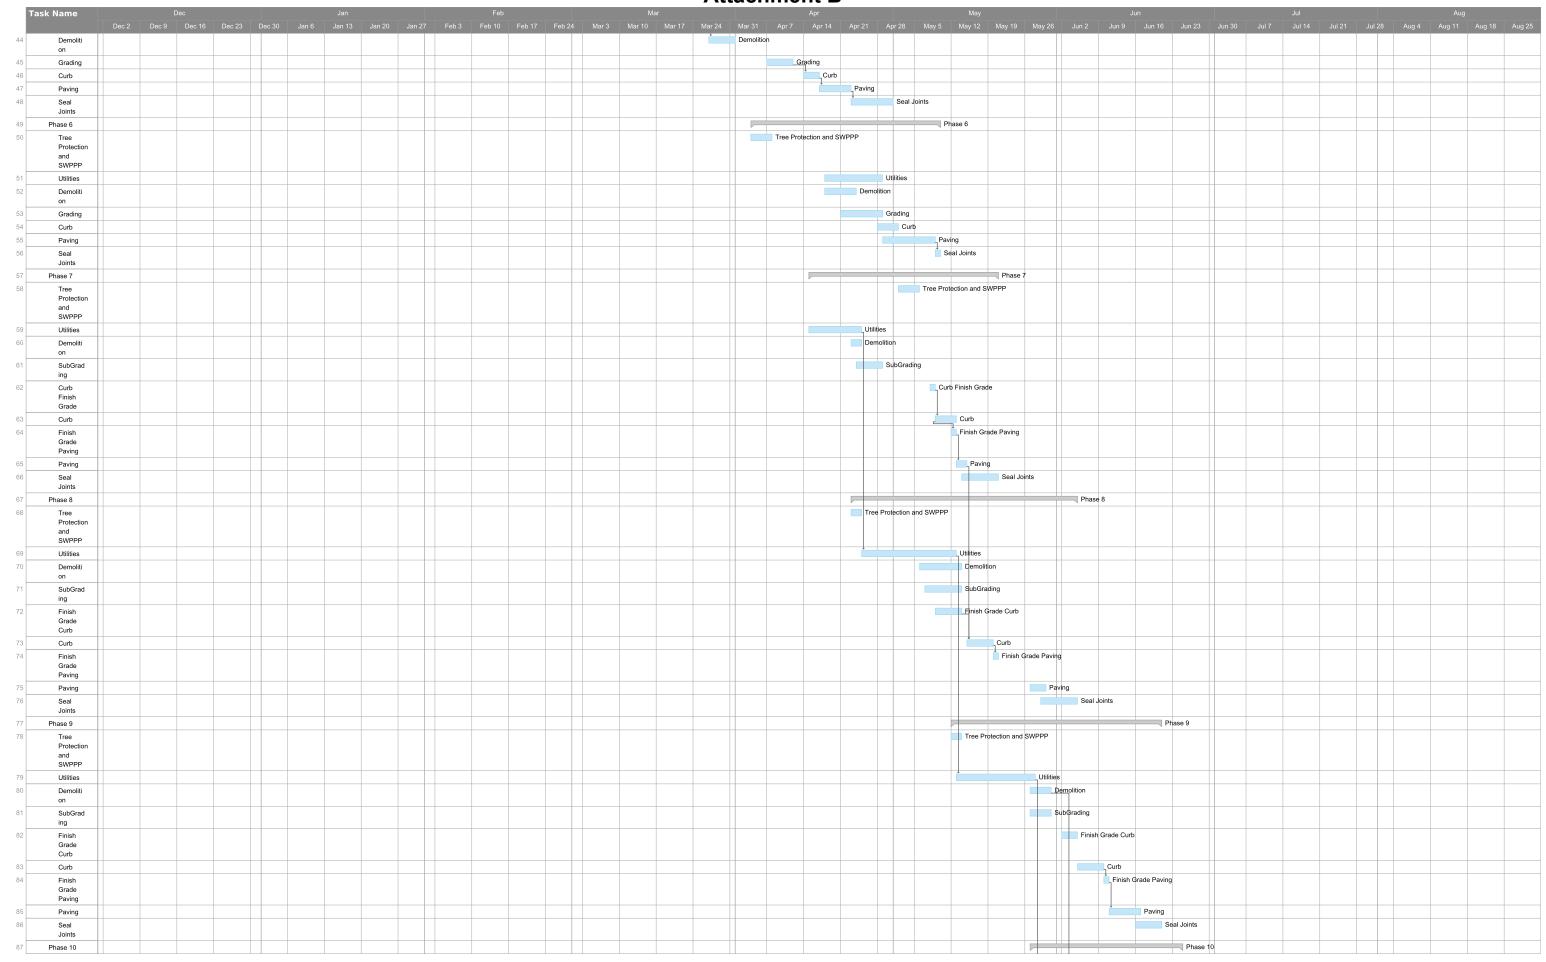

Attachment B

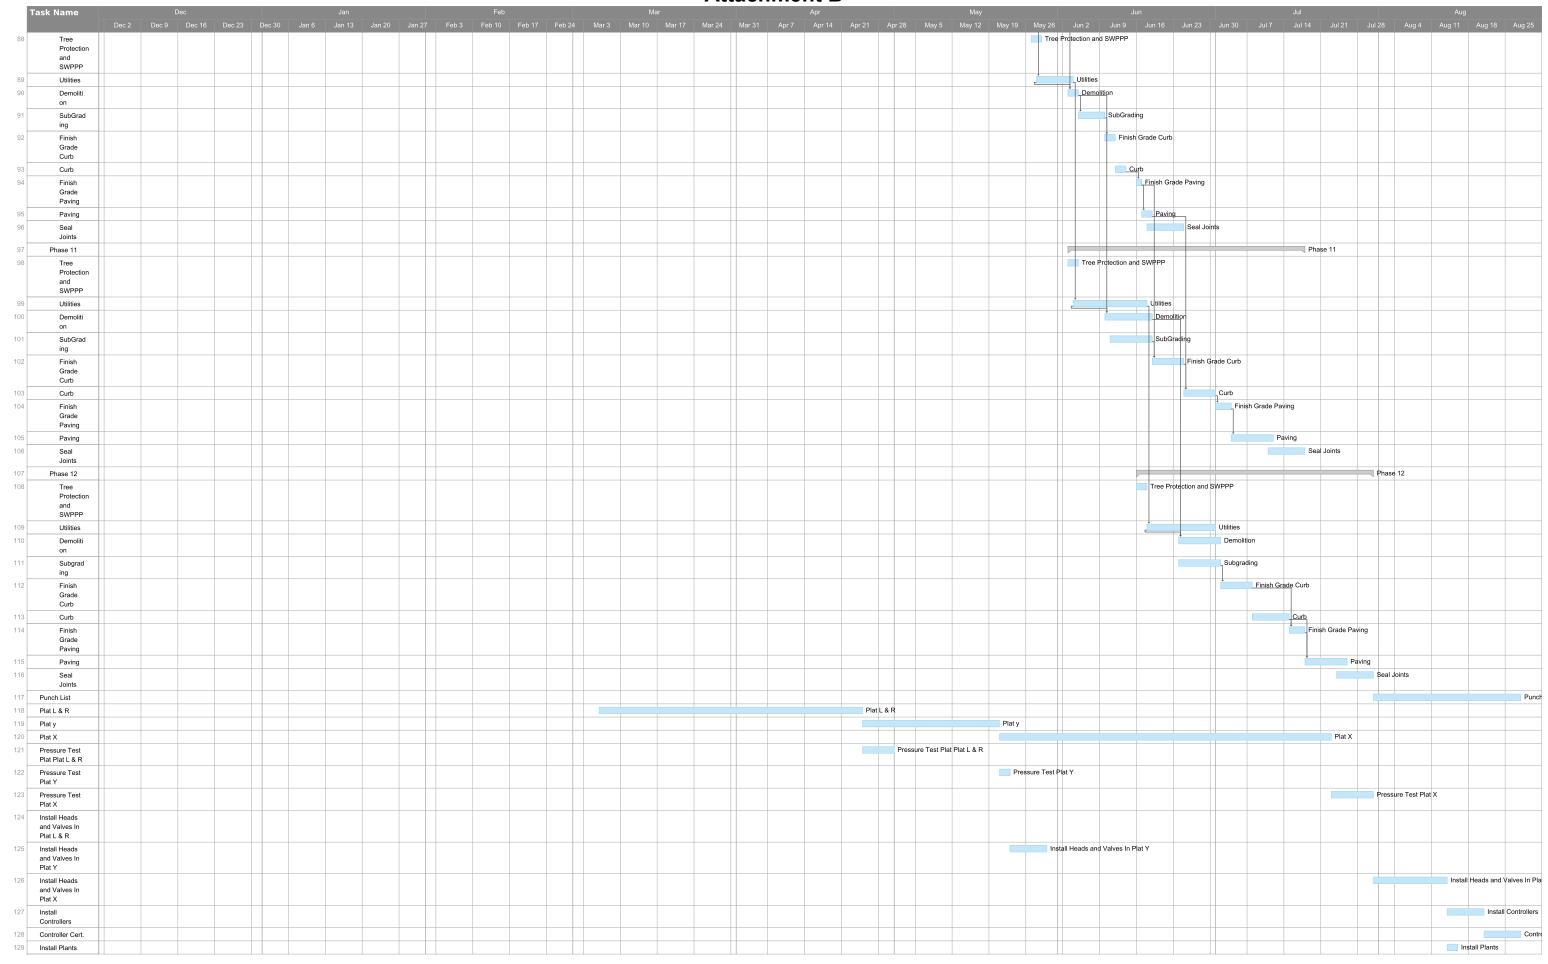

Attachment B

	Task Name		Оес		Jan				Jan Feb				Ma	ar		Apr				May				Jun				Jul					Aug					
			Dec 16	Dec 23 E	Dec 30			Jan 20			Feb 10 Feb	7 Feb 24				Mar 24	Mar 31	Apr 7	Apr 14	Apr 21	Apr 28	May 5		May 19	May 26				Jun 23				Jul 21	Jul 28			Aug 18 Aug	25
130	Install Mulch																																				Install Mulch	
131	Install Sod																																					_ Ins
132																																						

Exported on June 2, 2025 10:44:08 AM PDT

Page 4 of 4
