



ESTABLISHED 1957

## CITY CEMETERY ROADWAY & IRRIGATION IMPROVEMENTS

### SALT LAKE CITY PROJECT # PRK23013

## CONSTRUCTION GENERAL INFORMATION - (November 27, 2024) and CONSTRUCTION STATUS UPDATE NOTICE # 1 – (December 2, 2024)

**PLEASE BE ADVISED THAT CONSTRUCTION WILL BE OCCURRING at the Salt Lake City Cemetery.**

- The City Cemetery is generally between 11<sup>th</sup> Avenue and 4<sup>th</sup> Avenue, N Street and U Street.
- **THE PROJECT AREA is in the Cemetery's Northeast Quadrant, generally located between 1040 E. and 1200 E. and 280 N. and 11<sup>th</sup> Avenue (see the image on page 3/3).**

### **OVERALL PROJECT SCHEDULE: December 2024 – July 2026.**

- We anticipate construction beginning December 2024, with some mobilization beginning November 25-27, 2024.
- The estimated completion date of Work Sequence 1 (about 80% of the work) is Winter 2025.
- The estimated completion of Work Sequence 2 is Summer 2026.
- Anticipated hours of operation will generally be 7 AM to 6 PM Monday through Friday and Saturday 7 AM to 2 PM.
- \*\*Schedule is subject to change depending on weather, permitting, and unknown circumstances.

**GENERAL PROJECT WORK DESCRIPTION:** Tree protection and SWPPP, Demolition, Utilities (Roadway Irrigation and Plat Irrigation), Grading, Curb and Gutter, Concrete Paving, Landscape Restoration. Roadway improvements generally include replacing exiting roadway features with concrete pavement, curb and gutter, waterways, and street signs with decorative posts. Roadway area irrigation system improvements (roadway and roadway vaults and associated assemblies and electrical pipe, wiring, and controllers) generally include replacing irrigation with new irrigation system. Plat area irrigation system improvements generally include replace landscape irrigation and install new root watering system for trees, and related work.

### **WORK TO BE PERFORMED THIS WEEK AND NEXT WEEK:**

- Tree protection fencing controls and storm water controls, mobilization (equipment and associated items), grading at 325 N. 1125 E. for the construction yard (coordinated with the Catholic Cemetery).
- **Work will begin on 1040 E. the first week of December.** Demolition in the work area of Phase 1 highlighted in green in the image below is expected to begin Monday, December 2.

**IMPACT OUTSIDE CEMTERY:** The main impact to the surrounding residents beyond the Cemetery is construction noise. Water connection in 11<sup>th</sup> Avenue and associated work in spring 2025.

### **IMPACT TO CEMETERY: Construction noise, dust, vibration, road closures.**

- **If you have any special needs or need assistance that may be complicated by construction, please contact the Cemetery main office staff at 801-596-5020.**
- Burial services in the project area will be scheduled from 12-4PM.
- The Contractor will not operate heavy equipment in a plat or adjacent to a plat having a service.
- The contractor will not work on site the weekend prior to and on Memorial Day.

- Work schedules and sequences will modify for burials and other events on site. Work activities and schedules will be coordinated with the Owner and their burial/maintenance activities on site.

#### **TRAFFIC**

- Work will be in stages to provide continuous public usage.
- One side of every plat will maintain public accessibility.
- Two consecutive intersections will not be closed at any given time, except short term directional drilling operations.
- The main contractor access will be from 11<sup>th</sup> Ave. 1150 E.

We ask that you please keep a safe distance from any traffic barriers and are mindful of work zones for your safety.

\*All work is subject to change.

MC Green & Sons, Inc.

Any construction concerns or questions should be forwarded to the **contractor's representative Jason Draper, 801.870.4366, [jason@mcgreen.net](mailto:jason@mcgreen.net), copy Brian Whittam** (see the contact information below).

Salt Lake City Corporation, Engineering Division

**Brian Whittam, Project Management Consultant, MOCA Systems, Inc., Project Manager, 801-556-1570, [brian.whittam@mocasystems.com](mailto:brian.whittam@mocasystems.com)**

Hayden Barker, Engineering Construction Program/Project Manager, 385-530-5790 cell, [hayden.barker@slc.gov](mailto:hayden.barker@slc.gov)

Project Information can be found at: (website pending).


**Salt Lake City Corporation, Cemetery**

**Main office staff, 801-596-5020.**

Cemetery website: <https://www.slc.gov/parks/city-cemetery/>

**Thank you for your continued patience and support during this project construction.**

## PROJECT MAP AND PHASING/ZONING

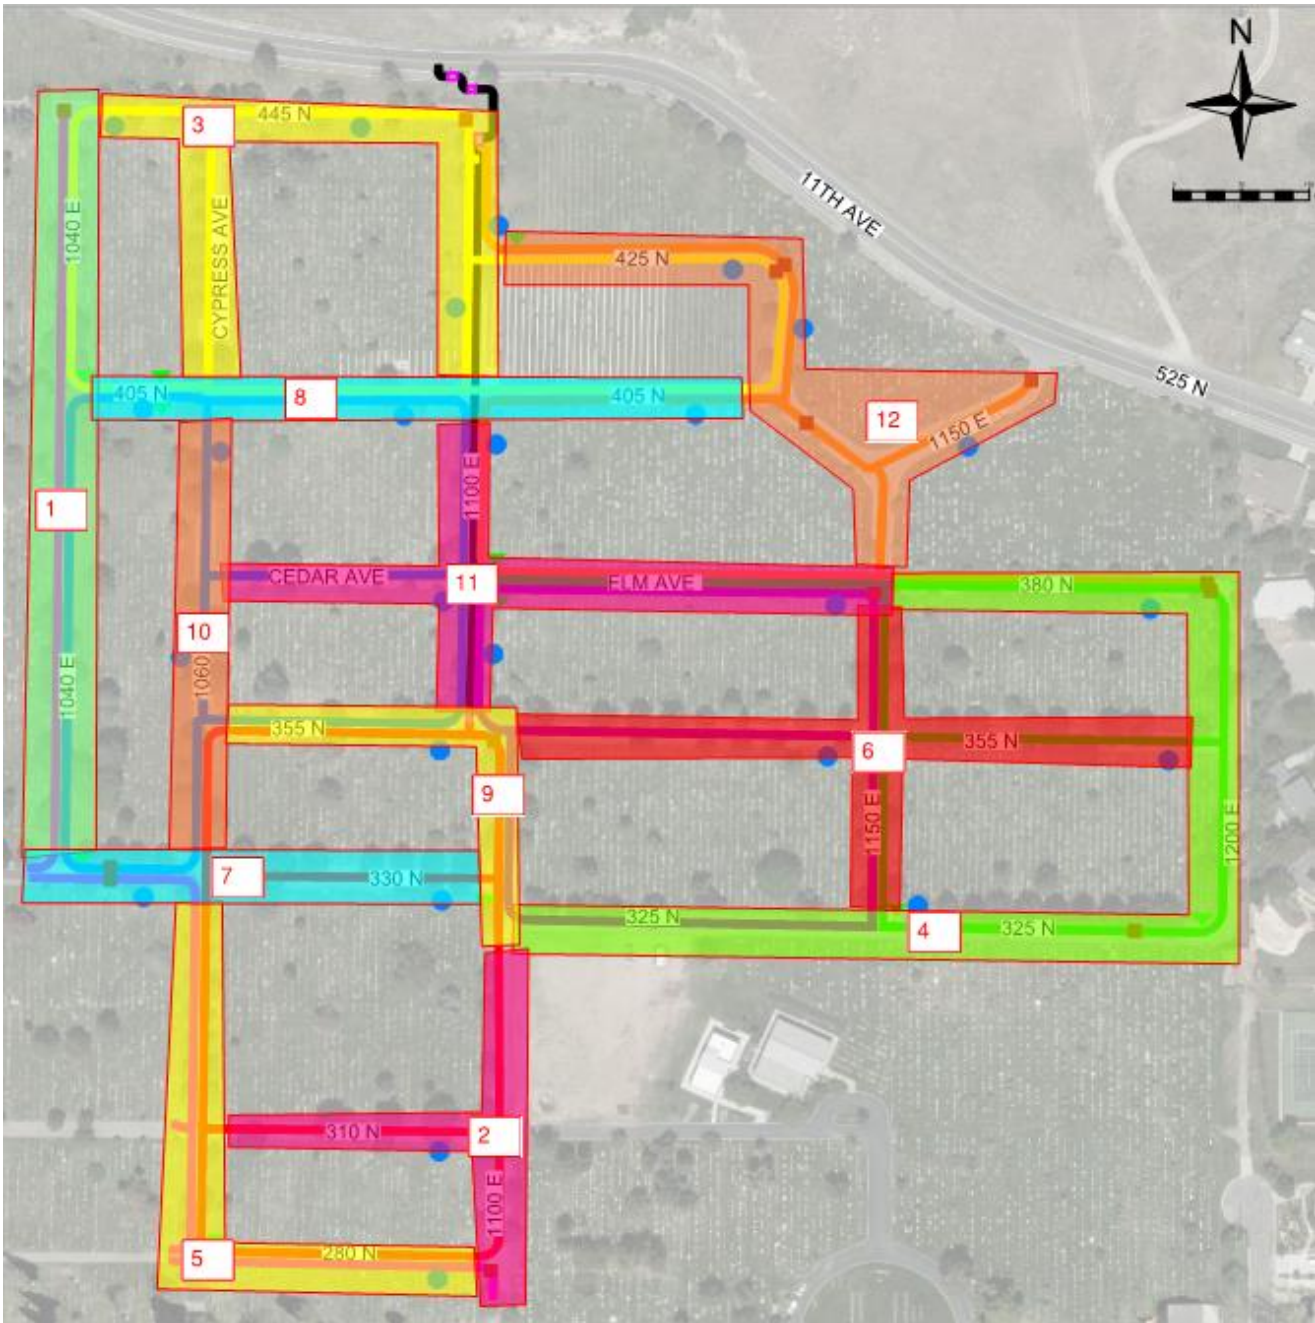

Preliminary Substantial Completion Phasing Schedule (subject to change). Not including punch list, changer order, contingency, or other work.

Phase 1: 12/03/24 to 1/03/25	Phase 7: 3/15/25 to 4/29/25
Phase 2: 12/07/24 to 1/21/25	Phase 8: 4/04/25 to 5/19/25
Phase 3: 12/27/24 to 2/10/25	Phase 9: 4/22/25 to 6/08/25
Phase 4: 1/14/25 to 3/02/25	Phase 10: 5/12/25 to 6/28/25
Phase 5: 2/03/25 to 3/22/25	Phase 11: 6/01/25 to 7/18/25
Phase 6: 2/23/25 to 4/11/25	Phase 12: 6/21/25 to 8/05/25
